PromptFunds

IMPLEMENTATION PLAN

Implementation Plan

Prompt Funds — phases, timeline, team, deliverables and go-live checklist


VERSION	DATE	PREPARED FOR	CLASSIFICATION
1	November 2026	Prompt Funds / cooperative lending clients	Confidential

1. Approach

Deliver in phases so the cooperative **accepts members' money only after the core ledger is proven**, and switches on digital lending only once savings operations are stable. The codebase already contains a working implementation of every phase-1 and phase-2 module; the plan below takes it from working software to a licensed, tested, live service.

Total time to savings launch: ~14 weeks. Lending live: ~20 weeks. Regulatory and banking workstreams (Phase 0) run in parallel with engineering.

2. Timeline

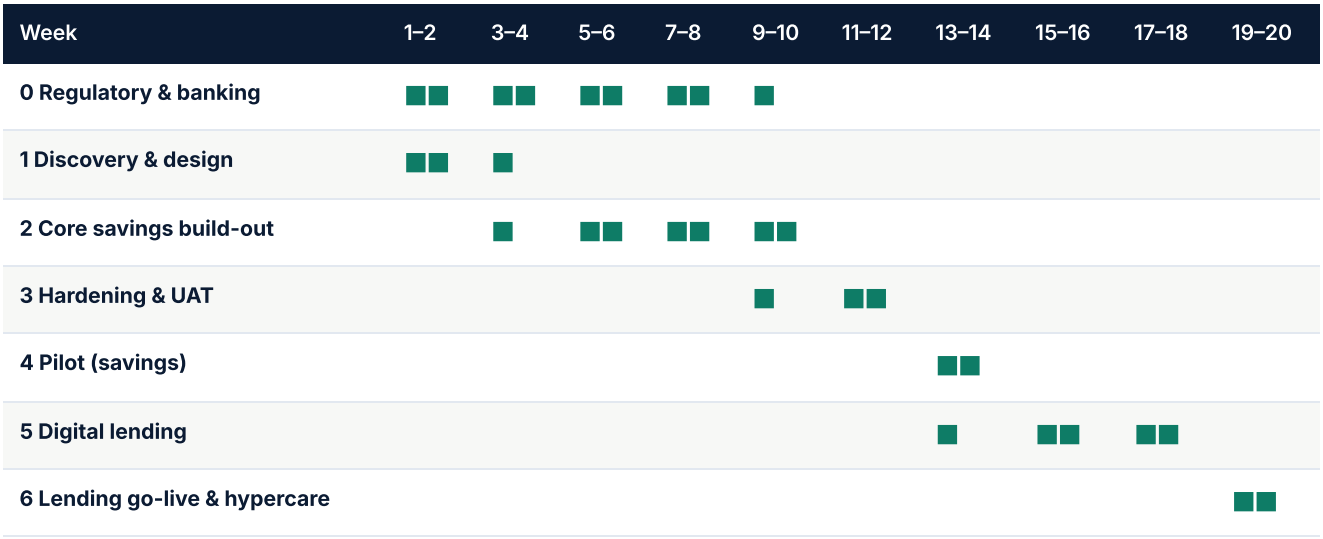

3. Phases and deliverables

Phase 0 — Regulatory, policy and banking (weeks 1–9, cooperative-led)

Activity	Owner	Deliverable
Confirm cooperative registration, by-laws allow digital membership and savings from members	Board + counsel	Legal opinion
Confirm lending licence scope; FCCPC registration/approval under the DEON Consumer Lending Regulations 2025 before digital loans launch	Counsel	Registration filed / approval
Approve savings, withdrawal, lending, provisioning, liquidity, investment and complaints policies	Board	Signed policy pack (rates, limits, SLAs)
Select payment partner; open collections and payouts accounts; sign DVA + transfers agreement; written confirmation the setup fits the licence	Finance	Live + test API keys
Select KYC provider; sign data processing agreement	Ops	Sandbox + live keys
NDPA 2023: privacy notice, DPIA, DPO, vendor DPAs	DPO	Compliance file

Activity	Owner	Deliverable
Terms of membership, loan agreement, key facts statement	Counsel	Approved documents (loaded into the app)

Phase 1 — Discovery and design (weeks 1–3)

- Workshops: confirm requirements in the PRD, staff roles, approval limits, report formats.
- Brand finalisation (logo, colours, tone) and content for public pages.
- Design review of all screens on real mid-range Android devices.
- **Deliverables:** signed-off PRD, clickable prototype (the running staging site), content deck, UAT plan.

Phase 2 — Core savings build-out (weeks 3–10)

The starter already implements registration, KYC, wallet, deposits, withdrawals, interest, admin queues and reports. Remaining work:

Workstream	Tasks
Integrations	Paystack live DVA + transfers in staging; Dojah live BVN; settlement-report reconciliation job + resolution UI
Security	Staff TOTP MFA; rate limiting (Upstash); CSP; session device list; payout-account change workflow with cooling-off
Notifications	SMS (Termii) + email (Resend) via post-commit queue; templates
Statements	PDF statement; monthly e-statement email
Admin	Policy editor with maker-checker; staff management; CSV/XLSX exports; board pack
Quality	Integration tests on a Postgres service container; Playwright end-to-end suite on mobile viewport; load test
Deliverables	Staging environment with live sandbox integrations; test reports; admin user guide

Phase 3 — Hardening and UAT (weeks 9–12)

- Financial UAT: 100 test wallets, interest independently recomputed in a spreadsheet, every posting traced to the ledger, trial balance ₦0.
- Concurrency tests: parallel withdrawals, webhook replays, job re-runs.
- External penetration test; fix all high/critical findings.
- Disaster-recovery drill: restore production snapshot to a branch, verify trial balance.
- Staff training (KYC, finance, admin) and runbooks.
- **Deliverables:** UAT sign-off, pen-test report and remediation evidence, DR drill record, runbooks.

Phase 4 — Savings pilot (weeks 13–14)

- Closed pilot with 50–200 members (staff, board, friendly members), real money with low limits (e.g. ₦200,000 balance cap, ₦50,000 daily withdrawal cap).
- Daily reconciliation review with finance; weekly steering meeting.
- **Go/no-go criteria:** zero unexplained variances for 10 consecutive business days; all withdrawals within SLA; no Sev-1 incidents.

Phase 5 — Digital lending (weeks 13–18)

Lending code is present; this phase activates it safely.

Task	Notes
Configure approved loan products, rates, fees, limits	From the board-approved lending policy
Loan agreement + key facts statement in the offer screen	Counsel-approved text
Credit policy rules tuning (affordability %, savings multiple, membership age)	Policy-driven settings
Disbursement through live transfers; failure reversal tested	Finance sign-off
Arrears process: reminders (SMS), collections scripts compliant with FCCPC rules	No contact-list access, no shaming
Provisioning: loss provision postings by ageing bucket (month-end)	Finance
FCCPC approval in hand	**Hard gate**
Lending UAT and pilot with capped amounts	20–50 loans

Phase 6 — Lending go-live and hypercare (weeks 19–20)

- Gradual limits increase; daily PAR and liquidity monitoring.
- 30-day hypercare: priority support, daily stand-up, weekly report to management.

4. Team

Role	FTE (build)	Responsibility
Product / delivery lead	0.5	Scope, priorities, stakeholder alignment, UAT
Senior full-stack engineer (Next.js/TypeScript)	1.0	Architecture, ledger, integrations, code review
Full-stack engineer	1.0	Features, admin portal, tests
UI/UX designer	0.5 (weeks 1–6)	Design system, prototypes, usability tests
QA engineer	0.5	Test plans, automation, financial UAT support
DevOps / security (part-time)	0.2	Environments, monitoring, secrets, pen-test liaison
Cooperative side	—	Product owner, finance lead, KYC lead, counsel, DPO

5. Governance

- **Weekly:** demo of working software on staging; risk and decision log reviewed.
- **Fortnightly:** steering committee (cooperative management + delivery lead).
- **Change control:** any change to money logic requires a written change request, test evidence, and finance sign-off.
- **Definition of done:** code reviewed, tests passing in CI, deployed to staging, acceptance criteria demonstrated, docs updated.

6. Risk register

Risk	Likelihood	Impact	Mitigation
Regulatory approval delayed (FCCPC / licence scope)	Medium	High	Start Phase 0 on day 1; launch savings first; lending behind feature gate
Payment partner onboarding slow	Medium	High	Shortlist two partners (Paystack, Monnify); adapter allows switching
Members misunderstand “wallet” as a bank account	Medium	Medium	Clear copy: members-only, no transfers, not NDIC-insured
Liquidity shortfall for withdrawals	Low	High	Liquidity cover KPI + alert; withdrawal SLA; investment policy limits
Loan defaults above plan	Medium	High	Conservative limits (3× savings, 40% affordability); auto-debit; provisioning
Fraud (identity, account takeover)	Medium	High	BVN match + duplicate hash; own-account payouts only; MFA; cooling-off on payout changes
Data breach	Low	High	Field encryption, least privilege, audit, pen test, NDPA processes
Key-person dependency	Medium	Medium	Documentation, runbooks, code in client-owned GitHub

7. Go-live checklist

- [ ] Legal opinion and FCCPC registration status documented
- [ ] Board-approved policies loaded (rates, limits, products) — placeholder seed values replaced
- [ ] Live payment and KYC keys in Netlify env vars; webhook URLs registered and tested
- [ ] `DEMO_MODE=false`, `KYC_AUTO_APPROVE` set per policy, strong `FIELD_ENCRYPTION_KEY`, `IDENTITY_HASH_SECRET`, `CRON_SECRET`
- [ ] Seed staff passwords changed; MFA enforced; leavers removed
- [ ] Scheduled function running; last accrual visible on Operations page
- [ ] Monitoring and alerts live (trial balance, job health, payout failures, uptime)
- [ ] Backups + PITR confirmed; restore drill passed
- [ ] Pen-test high/critical findings closed
- [ ] Support channels staffed; complaint process published
- [ ] Privacy notice, terms, loan agreement published

8. Post-launch roadmap

Quarter	Items
Q+1	Savings goals, PWA install prompt, referral programme, WhatsApp notifications

Quarter	Items
Q+2	Fixed-term deposits, guarantor loans, credit bureau, bank-statement analysis
Q+3	React Native app (iOS/Android) reusing the API, USSD for feature phones
Q+4	BI dashboards (Metabase), automated regulator returns, optional .NET reconciliation worker
